

WBV - 17b.2

STA. 160+00 TO HWY 90 - PHASE 2

Inspection Report


Date: 12/13/2010 **Start Time:** 1:45 PM **End Time:** 2:00 PM

Weather: Clear

Attendees: Chris Muscarello, Don Robertson

-
1. WBV-17b.2 Hwy 90 to Lake Cataouatche Pumping Station Levee
Contractor: Healtheon
Contract Award Date: 2-Nov-10
Substantial Completion Date: 21-Aug-11
Contract Value: \$5,302,090
Job is 0% complete.

This project consists of raising the elevations of approximately 1 mile of earthen levee that was constructed during Phase 1 to the 100 year level of protection. This contract will involve the levee that parallels a landfill that lies south of Highway 90 as part of the Lake Cataouatche system in Jefferson Parish.

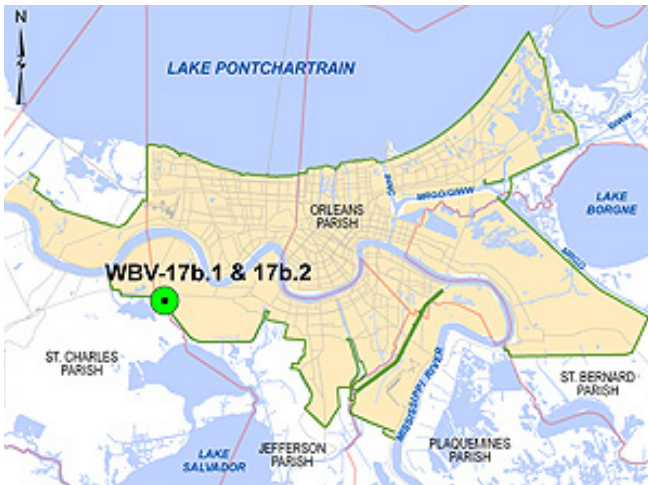

2. Contractor has not yet mobilized to site.





Inspector Name(s)

Chris Muscarello

Inspector Signature(s)

Signature on file
